



WORKS DEPARTMENT
Development Works
of
DHENKANAL (R&B) DIVISION



ONGOING BRIDGE PROJECTS



Construction of H.L.Bridge over river Brahmani near Badakhamar on Khadagprasad Badakhamar Pangatira Road (RIDF-XXVI).

A/A Details	:-	Rs.11,491.58 Lakh vide Letter No 13760 dtd. 09.11.2020 by Works Deptt.
Length of Bridge	:-	19 x 62.07 = 1179.33 m
Agreement Cost	:-	Rs. 9136.47 Lakhs (Including GST)
DOC/SDOC	:-	28.07.2021/ 27.01.24 Appointment date 30.10.2022
Target Date of Completion	:-	31.03.2026
Up to date expenditure	:-	Rs.9112.06 Lakhs (Including GST)
Physical Progress	:-	Pile Foundation- 102 nos/102 nos Pile Cap- 20 nos/20 nos Pier Shaft- 18nos/18 nos Pier cap-18 nos/18 nos Abutment Shaft- 2nos/2 nos Abutment cap -2 nos/2 nos Dirt Wall - 0/2nos Wing Wall and Return Wall - 0/2nos Pedestals-76 nos/76 nos Supply & Fabrication Bearings- 76nos/76 nos Bearing Fixation- 8/76nos PSC Box Segments Pre Casting- 335/361 PSC Box Segments-Launching-7/19 Span
Issues or Bottleneck if any	:-	



Construction of H.L Bridge over Urbengi nala at 14.05 km. Kamakhyanagar to Kankadahad road under state plan.

A/A Details	:-	Rs.833.57 Lakhs vide Letter No 7556 dtd. 24.02.2023 of EIC (Civil) Odisha
Length of Bridge	:-	4x19.36 = 77.44 m
Agreement Cost	:-	Rs. 728.93 Lakhs (Including GST)
DOC/SDOC	:-	25.04.2023 / 24.03.2024
Target Date of Completion	:-	31.01.2026
Up to date expenditure	:-	Rs.404.30 Lakhs (Including GST)
Physical Progress	:-	4 spans of 19.36 mtr each Pile Foundation- 5 Nos/5 Nos Pile Cap-- 5 Nos/5 Nos Pier Shaft- 3 Nos/3 Nos Abutment Shaft- 2 Nos/2 Nos Pier Cap- 3/3 Nos Abutment Cap- 2/2 Nos Girder - 12/16 Nos Deck Slab -0/ 4 Nos
Issues or Bottleneck if any	:-	



Construction of HL Bridge over river Ramial at 18th km on Khatakhura PWD road via Bhairpur Panchayat, Santarpur-Bankualo-Sana Brahmapur-Balisahi to Lokanathpur Flood Embankment to Baligorada-Motta-Jodapal Chhacka in the district of Dhenkanal under State Plan for the year 2023-24..

A/A Details	:-	Rs.2908.68.00 lakhs vide Letter No 3638 dtd. 26.02.2024 of Works deptt, Odisha
Length of Bridge	:-	4x30M =120M
Agreement Cost	:-	Rs. 2556.75 Lakhs (Including GST)
DOC/SDOC	:-	22.02.2024 / 21.08.2026
Target Date of Completion	:-	21.08.2026
Up to date expenditure	:-	Rs.651.62 Lakhs (Including GST)

Physical Progress	:-	<p>BBridge Proper. 4 spans of 30 mtr c/c each</p> <p>Well Foundation</p> <p>i.Abutment well cap- 2 Nos /2 Nos.</p> <p>ii. Pier well cap - 0 Nos / 3Nos</p> <p>iii.Abutment Shaft- 0 Nos/2 No</p> <p>iv.pier- 0 Nos/ 3 No</p> <p>vi. Abutment Cap- 0 Nos /2 No</p> <p>vii.Pier Cap- 0 Nos/3 No</p> <p>viii.AL Well - 12 Mtr/12 Mtr</p> <p>ix.AR - 3.2 mtr/10 Mtr</p> <p>x.P1 - 11.7 Mtr/11.70 Mtr</p> <p>xi.P2 - 9.90 Mtr/9.90 Mtr</p> <p>xii.P3 - 10.50 Mtr/10.50 Mtr</p>
-------------------	----	---

Issues or Bottleneck if any	:-	
-----------------------------	----	--



Construction of HL Bridge over river Ramial at 8th km on Khatakhura PWD road via Bhairpur Panchayat, Santarpur-Bankualo-Sana Brahmapur-Balisahi to Lokanathpur Flood Embankment to Baligorada-Motta-Jodapal Chhacka in the district of Dhenkanal under State Plan for the year 2023-24.

A/A Details	:-	Rs.5174.00 lakhs vide Letter No 3650 dtd. 26.02.2024 of Works deptt, Odisha
Length of Bridge	:-	10x30M =300M
Agreement Cost	:-	Rs. 4562.35 Lakhs (Including GST)
DOC/SDOC	:-	26.02.2024 / 25.08.2026
Target Date of Completion	:-	25.08.2026
Up to date expenditure	:-	Rs.679.36 Lakhs (Including GST)
Physical Progress	:-	<p>Bridge Proper. 2 spans of 29.96 c/c mtx10 Span each Pile Foundation i.Abutment - 2 Nos /2 Nos. ii. Pier - 9 Nos / 9Nos iii.Pier Shaft- 0 Nos/9 No iv.Abutment Shaft- 0 Nos/ 2 No vi. Pile Cap- 0 Nos /11 No vii.Pier Cap- 0 Nos/9 No viii. Abutment Cap- 0 Nos/2 No ix.Deck Slab - 10 x29.96m</p>
Issues or Bottleneck if any	:-	



Construction of H.L Bridge over Dhania Nallah at 2/970 km of Sadangi-Nihalprasad road in the district of Dhenkanal under state plan for the year 2023-24.

A/A Details	:-	Rs.973.22 vide Letter No 29912 dtd. 19.07.2023 of E.I.C (Civil), Odisha
Length of Road	:-	40.00 M
Agreement Cost	:-	Rs. 827.00 Lakhs (Including GST)
DOC/SDOC	:-	16.10.2023 / 15.09.2024
Target Date of Completion	:-	31.12.2025
Up to date expenditure	:-	Rs.550.19 Lakhs (Including GST)
Physical Progress	:-	<ol style="list-style-type: none"> 1. Pile - 22 nos/22 nos 2. Pile Cap- 3 nos/3 nos 3. Pier Shaft- 2nos/2 nos 4.Pier cap-1 nos/1 nos 5.Abutment Shaft- 2nos/2 nos 6.Abutment cap -2 nos/2 nos 7.Return Wall - 0/4nos 8.Pedestals-12 nos/12 nos 9.RCC Retaing Wall- 120/120 Rmt 10.Girder -4/4 nos 11. Toe wall 966/1563 Rmt 12. RCC Slab - 2/2 Span Completed
Issues or Bottleneck if any	:-	





ONGOING ROADS PROJECTS



Improvement to Bhalumunda to Saranga road from 0/0 Km to 10/0Km in the District of Dhenkanal under State Plan

A/A Details	:-	Rs.1295.60 vide Letter No 2699 dtd. 17.02.2023 of Works deptt, Odisha
Length of Road	:-	10.000 Km
Agreement Cost	:-	Rs. 1137.89 Lakhs (Including GST)
DOC/SDOC	:-	15.03.2023 / 14.12.2023
Target Date of Completion	:-	30.11.2025
Up to date expenditure	:-	Rs.963.57 Lakhs (Including GST)
Physical Progress	:-	<ul style="list-style-type: none"> i.Widening With GSB- 6313 mtr/6313 mtr ii.Widening With WMM -6012/6313 mts iii.Overlaying With WMM - 6012/6313mts iv.Overlaying With BM- 6091/6313 mts v.Overlaying With SDBC- 6091/6313 mts vi.Overlaying with DLC-0/315mts vii.Overlaying with PQC- 2227/2875mts viii.Concrete drain-0/865mts ix.Retaing Wall- 241/395mts x.Toe Wall- 40/240mts xi.Reconstruction with HPC (Single Row)- 16/19 nos
Issues or Bottleneck if any	:-	



Widening & strengthening of Deogan-Mandar Road from 0/0 Km to 21/200 Km in the District of Dhenkanal under CRIF

A/A Details	:-	Rs.2695.16 vide Letter No 31935 dtd. 22.08.2022 of o/o E.I.C, Odisha
Length of Road	:-	21.200 Km
Agreement Cost	:-	Rs. 2385.35 Lakhs (Including GST)
DOC/SDOC	:-	15.03.2023 / 14.11.2024
Target Date of Completion	:-	30.12.2025
Up to date expenditure	:-	Rs.2035.06 Lakhs (Including GST)

i. Widening with GSB=19.7km/21.20km

ii. WMM=19.7km/21.20km

Physical Progress :- BM=19.7km/21.20km

iii.

iv. Overlaving BC=19.70 Km/21.20



Improvement to such as Widening & Strengthening of Karmula-Mandar Road from 0/0 km to 12/400 km for the year 2022-23 .

A/A Details	:-	Rs.1235.34 vide Letter No 4274 dtd. 31.03.2021 of Works Deptt., Odisha
Length of Road	:-	12.400 Km
Agreement Cost	:-	Rs. 1163.09 Lakhs (Including GST)
DOC/SDOC	:-	28.07.2022 / 27.07.2023
Target Date of Completion	:-	30.12.2025
Up to date expenditure	:-	Rs.661.28 Lakhs (Including GST)
Physical Progress	:-	<ol style="list-style-type: none"> 1. Widening with GSB=9.2km/11.574km 2. WMM=9.2km/11.574km 3. Overlaying WMM=9.20km/11.574km 4. BM=8km/11.574km 5. BC=8km/11.574km 6. CC Pavement=150mtr/793mtr 7. RCC Drain=0/176mtr 8. CD=18nos/40nos 9. RCC Wall =0/60mtr 10. Saucer Drain= 0/1.59 Km
Issues or Bottleneck if any	:-	



Improvement such as widening & strengthening to defunct NH-53 from 384/700 Km to 387/200 Km inside Bhuban under State Plan

A/A Details	:-	Rs.1178.60 vide Letter No 15583 dtd. 04.11.2022 of Works deptt, Odisha
Length of Road	:-	3.5 Km
Agreement Cost	:-	Rs. 983.33 Lakhs (Including GST)
DOC/SDOC	:-	20.04.2023 / 19.07.2024
Target Date of Completion	:-	31.03.2026
Up to date expenditure	:-	Rs.593.38 Lakhs (Including GST)
Physical Progress	:-	<ol style="list-style-type: none"> 1.GSB Widening - 2.3/2.500 Km 2.WMM Widening - 2.3/2.500 Km 3.WMM overlaying - 2.418/2.5 Km 4.DBM Gr - II - 2.6/2.60 Km 5.BC Gr-II 0/2.5 Km 6.HPC - 0/12 Nos 7.RCC BOX - 2/2 Nos 8.Toe wall - 119/180 Mtr 9.Drain - 2220/5000 Mtr
Issues or Bottleneck if any	:-	



Improvement such as widening and strengthening of Hindol NAC to Sinkola village road from 0/000 km to 8/700 km in the district of Dhenkanal under State Plan

A/A Details	:-	Rs.1857.20 lakhs vide Letter No 12226 dtd. 25.07.2023 of Works deptt, Odisha
Length of Road	:-	8.700 Km
Agreement Cost	:-	Rs. 1502.33 Lakhs (Including GST)
DOC/SDOC	:-	30.11.2023 / 29.11.2024
Target Date of Completion	:-	31.03.2026
Up to date expenditure	:-	Rs.1188.89 Lakhs (Including GST)

- i) GSB VI Widening - 3644m/3644 m.
- (ii) WMM Widening -3644m/ 3644 m.
- (iii)GSBVI overlaying-2789m/2789m
- (iv) WMM Overlaying-6433m/ 6433 m.
- (v) BM overlaying -6433m/ 6433 m.

(vi)SDBC overlaying --6433m/ 6433

m.

(vii) CC Road-528m/241m

(viii) HP Culvert New-3 Nos/3 Nos

(ix)HP culvert widening-11 Nos/13Nos

Physical Progress :-



Improvement such as widening and strengthening of Old NH-42 (Meramundali Bazar) to Kamalanga via Khadagaprasad from 0/000 km to 12/800 km (except 63m Railway portion) in the district of Dhenkanal under State Plan

A/A Details	:-	Rs.2038.57 lakhs vide Letter No 12001 dtd. 20.07.2023 of Works deptt, Odisha
Length of Road	:-	12.170 Km
Agreement Cost	:-	Rs. 1759.29 Lakhs (Including GST)
DOC/SDOC	:-	30.11.2023 / 29.02.2025
Target Date of Completion	:-	31.03.2026
Up to date expenditure	:-	Rs.1258.15 Lakhs (Including GST)

- i) GSB Widening -8220m/9400 m.
- (ii) WMM Widening -8220m/9400 m.
- (iii) WMM Overlaying-8220m/9400 m.
- (iv) BM overlaying -8020m/9400 m.

(v)SDBC

- overlaying --7200m/9400 m.
- (vi) CC Road-325m/1024m
- (vi) HP Culvert-12Nos/11 Nos
- (vii)HP culvert widening-2 Nos/2Nos

Physical Progress :-



Improvement such as widening and strengthening to Letheka-Laulai road from 0/000 km to 6/466 km in the district of Dhenkanal under State Plan

A/A Details	:-	Rs.1281.26 vide Letter No 37607 dtd.07.09.2023 of E.I.C (Civil), Odisha
Length of Road	:-	6.466 Km
Agreement Cost	:-	Rs. 1131.37 Lakhs (Including GST)
DOC/SDOC	:-	13.12.2023 / 12.11.2024
Target Date of Completion	:-	30.12.2025
Up to date expenditure	:-	Rs.810.16 Lakhs (Including GST)
Physical Progress	:-	<ol style="list-style-type: none"> 1.Overlaying with GSB=5.540km/6.456km 2.WMM=5.540km/6.456km 3.BM=5.440km/6.456km 4. BC=5.440km/6.456km 5.RCC Drain=640mtr/960mtr 6.CD=22nos/22nos 7. RCC Wall =78mtr/78mtr 8. PCC Toe Wall- 112mtr/112mtr Completed.
Issues or Bottleneck if any	:-	



Improvement such as widening and strengthening of Tilapada to Kaluria road via Mohapada from 0/000 km to 9/186 km in the district of Dhenkanal under State Plan

A/A Details	:-	Rs.1857.68 vide Letter No 37406 dtd.05.09.2023 of E.I.C (Civil), Odisha
Length of Road	:-	9.186 Km
Agreement Cost	:-	Rs. 1522.80 Lakhs (Including GST)
DOC/SDOC	:-	19.01.2024 / 18.01.2025
Target Date of Completion	:-	31.12.2025
Up to date expenditure	:-	Rs.137.15 Lakhs (Including GST)
Physical Progress	:-	<ol style="list-style-type: none"> 1.Widening with GSB=3.5km/8.667km 2.WMM=3.5km/8.667km 3.Overlaying WMM=1.107km/8.667km 4.BM=0/8.667km 5.BC=0/8.667km 6.CC Pavement=0/500mtr 7. RCC Drain=0/1025mtr 8.CD=0/28nos 9.PCC Toe Wall =0/642mtr.
Issues or Bottleneck if any	:-	



Improvement of Chaulia High School PWD road to Kaluria Bridge via Khamara-Tavapal-Sundarpada-Anala-Radhadeipur and Latadeipur flood embankment road from 0/000 km to 17/261 km in the district of Dhenkanal under State Plan

A/A Details	:-	Rs.4577.59 vide Letter No 38347 dtd.11.09.2023 of E.I.C (Civil), Odisha
Length of Road	:-	17.261 Km
Agreement Cost	:-	Rs. 3861.31 Lakhs (Including GST)
DOC/SDOC	:-	12.12.2023 / 11.06.2025
Target Date of Completion	:-	31.12.2025
Up to date expenditure	:-	Rs.1725.91 Lakhs (Including GST)
Physical Progress	:-	<ol style="list-style-type: none"> 1. Overlaying with GSB=8.90km/16.255km 2. WMM=8.90km/16.255km 3. BM=8150/16.255km 4. BC=0/16.255km 5. CC Pavement=870mtr/891mtr 6. CD=18nos/28nos 7. Embankment Work= 10.00 km/16.37 km 8. PCC Toe Wall- 0/632mtr 9. RCC Drain=0/850mtr
Issues or Bottleneck if any	:-	



Improvement such as widening and strengthening of Khatakhura PWD road via Bhairpur Panchayat, Santarpur-Bankualo-Sana Brahmapur-Balisahi to Lokanathpur Flood Embankment to Baligorada-Motta-Jodapal Chhacka PWD road from 0/0 km to 23/950 km (except 7/400 km to 8/720 km, 17/600 km to 18/332 km, 15/705 km to 16/335 km) in the district of Dhenkanal under State Plan

A/A Details	:-	Rs.4232.68 lakhs vide Letter No 1208 dtd. 18.01.2024 of Works deptt, Odisha
Length of Road	:-	21.268 Km
Agreement Cost	:-	Rs. 3613.57 Lakhs (Including GST)
DOC/SDOC	:-	12.02.2024 / 11.01.2026
Target Date of Completion	:-	11.01.2026
Up to date expenditure	:-	Rs.2420.35 Lakhs (Including GST)
Physical Progress	:-	I. 1.GSB - 15.300/21.198 Km II. 2.WMM -15.000/21.198 Km III. 3.BM - 9.000/21.198 Km IV. 4.SDBC - 6.00/21.198 Km V. 5.PQC - 750 mtr/1073.Mtr VI. 6.HPC - 10 Nos/14 Nos VII. 7.BOX - 5 Nos/5 Nos VIII. 8.Toe Wall - 795/795.00 mtr IX. 9.Drain - 100/2036 Mtr
Issues or Bottleneck if any	:-	



Improvement such as widening and strengthening of Dhenkanal- Deogan- Haripur Road from 8/700 km to 21/500 km in the district of Dhenkanal under State Plan

A/A Details	:-	Rs.2633.85 lakhs vide Letter No 2761 dtd.08.02.2024 of Works deppt, Odisha
Length of Road	:-	12.800 Km
Agreement Cost	:-	Rs. 2161.09 Lakhs (Including GST)
DOC/SDOC	:-	13.12.2023 / 12.03.2025
Target Date of Completion	:-	31.12.2025
Up to date expenditure	:-	Rs.1135.87 Lakhs (Including GST)
Physical Progress	:-	<ol style="list-style-type: none"> 1.Widening with GSB=7.30km/12.80km 2. WMM=7.30km/12.80km 3.Overlaying BM=4.9km/12.80km 4.BC=3.00Km/12.80km 5.CD=3nos/10nos 6. PCC Toe Wall- 0/420mtr 7.RCC Drain=0/140mtr 8.Saucer Drain=0/2350mtr.
Issues or Bottleneck if any	:-	



Improvement such as widening and strengthening of Lokanathpur - Birasal Road from 0/000 km to 7/950 km (except 6/955 km to 7/010 km) in the district of Dhenkanal under State Plan

A/A Details	:-	Rs.1598.26 vide Letter No 39374 dtd.16.09.2023 of E.I.C (Civil), Odisha
Length of Road	:-	7.895 Km
Agreement Cost	:-	Rs. 1347.25 Lakhs (Including GST)
DOC/SDOC	:-	29.01.2024 / 28.12.2024
Target Date of Completion	:-	31.12.2025
Up to date expenditure	:-	Rs.138.95 Lakhs (Including GST)
Physical Progress	:-	<ul style="list-style-type: none"> 1.GSB widening - 4.5/7.577 Km 1.WMM widening - 4.5/7.577 Km 3.WMM Over laying - 0/7.577 Km 4.BM Gr-II -0/ 7.577 Km 5.SDBC Gr -II - 0/7.577 Km 6.PQC -0/ 290 Mtr 7.Box Cell - 0/12 Nos 8.Drain - 0/380 Mtr 9.Toe wall - 0/110 Mtr
Issues or Bottleneck if any	:-	



Improvement such as widening and strengthening of Dhenkanal-Kaimati-Joranda road from 0/800 km to 8/700 km & Dhenkanal-Deogaon-Haripur Road from 0/000 km to 14/955 km in the district of Dhenkanal under State Plan

A/A Details	:-	Rs.6665.17 vide Letter No 55248 dtd.26.12.2023 of E.I.C (Civil), Odisha
Length of Road	:-	22.855 Km
Agreement Cost	:-	Rs. 5218.77 Lakhs (Including GST)
DOC/SDOC	:-	04.03.2024 / 03.03.2025
Target Date of Completion	:-	31.12.2025
Up to date expenditure	:-	Rs.4106.47 Lakhs (Including GST)
Physical Progress	:-	<ol style="list-style-type: none"> 1.Widening GSB =14.955km/14.955km 2.WMM = 14.955km/14.955km 3. Overlaying GSB = 7.90km/7.90km 4.W.M.M = 22.055km/22.655km 5.D.B.M = 22.055km/22.655km 6.B.C. = 20.873Km/22.655km 7.CC Pavement = 0/200mtr 8.CD = 7nos/14nos. (2nos. in progress) 9.PCC Toe Wall- 0/420mtr. 10. RCC Drain=4373/6000mtr. 11.RCC Wall=436/520mtr.
Issues or Bottleneck if any	:-	




Construction of left side long approach road of Mahima Setu (At Kaluria) From Goradia to Gobindapur from 0/0 km to 5/400 Km in the district of Dhenkanal for the year 2023-24

A/A Details	:-	Rs.2348.93 vide Letter No 47761 dtd.13.11.2023 of E.I.C (Civil), Odisha
Length of Road	:-	5.330 Km
Agreement Cost	:-	Rs. 2060.81 Lakhs (Including GST)
DOC/SDOC	:-	15.03.2024 / 4.05.2025
Target Date of Completion	:-	31.12.2025
Up to date expenditure	:-	Rs.533.67 Lakhs (Including GST)
Physical Progress	:-	<ol style="list-style-type: none"> 1.Overlaying with GSB=0/5.33km 2.WMM=0/5.33km 3.BM=0/5.33km 4.BC=0/5.33km 5.CD=9nos/10nos 6.PCC Toe Wall- 720mtr/1100mtr 7. Earth in Embankment-4600/5330km
Issues or Bottleneck if any	:-	



Improvement to Badajhara-Bhairpur-NH-53, Right side of Rengali left canal up to Siarimalia & right side of Bharpur Distributary of Rengali Left Canal from Siarimalia to Dhenkanal- Kamakhyanagar road from Ch-0/000km to 19/500km

A/A Details	:-	Rs.3918.70 vide Letter No 17375 dtd.24.10.2024 of Works Dept
Length of Road	:-	19.500 Km
Agreement Cost	:-	Rs. 3108.58 Lakhs (Including GST)
DOC/SDOC	:-	10.01.2025 / 09.09.2026
Target Date of Completion	:-	09.09.2026
Up to date expenditure	:-	Rs.855.65 Lakhs (Including GST)
Physical Progress	:-	<ol style="list-style-type: none"> 1.Widening:- 0/12.544 km 2.Reconstruction:-0/6.643 Km 3.Widening GSB VI:-6.200 Km/12.544Km 4. Reconstruction GSB VI:-6.2 Km/6.643Km 5.2.Widening WMM :-6.200 Km/12.544Km 6.Reconstruction WMM VI:-6.2 Km/6.643Km 7. BM :-0.00 Km/19.187Km 8. SDBC :-0.00 Km/19.187Km 9.Protection Wall:- 0.00 Km/0.300Km 10.. Box Culvert 2x4X2 :- 0 No/1No 11. Toe Wall:-140 mtr/300m
Issues or Bottleneck if any	:-	

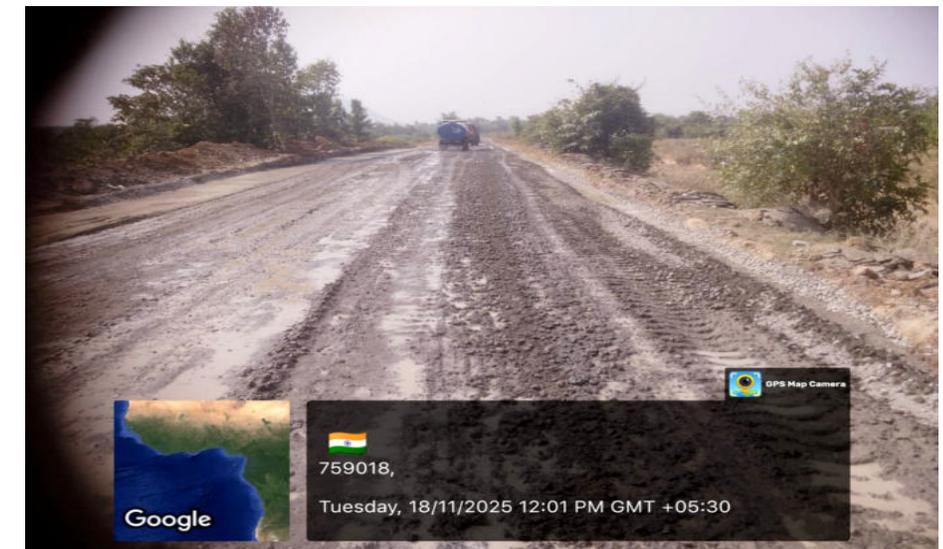

Improvement such as Widening & strengthening of Khatakhura- Bhairpur Road from Ch. 0/00 km to 15/875 km

A/A Details	:-	Rs.3791.75 vide Letter No 20129 dtd.04.12.2024 of Works Dept.
Length of Road	:-	16.016 Km
Agreement Cost	:-	Rs. 3086.05 Lakhs (Including GST)
DOC/SDOC	:-	11.04.2025 / 10.09.2026
Target Date of Completion	:-	10.09.2026
Up to date expenditure	:-	Rs.602.19 Lakhs (Including GST)
Physical Progress	:-	<ul style="list-style-type: none"> i. Widening With GSB for BT- 9706/12447 mtr ii. Widening with WMM- 9706/12447mtr iii.Overlaying With WMM - 0/12447mtr iv.Overlaying With BM- 0/12447 mts v.Overlaying With SDBC-0/12447 mts vi.Widening With GSB for CC - 0/3298 mtr vii.Widening With DLC- 0/3298 mts viii.Overlaying with PQC- 0/3298 mts ix.Retaing Wall- 0/500mts
Issues or Bottleneck if any	:-	



Improvement such as Widening & strengthening of Barihapur- Basoi- Kankli Sanda from Km. 0/000 to 5/570 Km

A/A Details	:-	Rs.1262.58 vide Letter No 20254 dtd.05.12.2024 of Works Dept.
Length of Road	:-	6.000 Km
Agreement Cost	:-	Rs. 1013.63 Lakhs (Including GST)
DOC/SDOC	:-	21.05.2025 / 20.11.2025
Target Date of Completion	:-	20.11.2025
Up to date expenditure	:-	Rs.0 Lakhs (Including GST)
Physical Progress	:-	Both side 1300 Mtr widening Exacavition and GSB work in completed
Issues or Bottleneck if any	:-	





COMPLETED PROJECTS



Construction of H.L. Bridge over River Brahmani near village Kaluria Saradeipur in Dhenkanal District (Mahima Setu)

Key Features:	<ul style="list-style-type: none"> Span Arrangement: 30 x 62.07 m = 1862.10 Mtr
Project Cost:	258.63 Crores
Completion Date:	31.03.2023
Agency:	<ul style="list-style-type: none"> M/S S.P Singhal Construction PVT LTD
Benefits of Project:	<p>*Due to construction of this bridge , the communication between Kaluria of Dhenkanal Assembly Constituency and Saradeipur of Kamakshyanagar Assembly Constituency developed .</p> <ul style="list-style-type: none"> The distance of about 16.00 Km has been reduced . About 62 villages with population 2.00 Lakhs benefited. Also it provides connection to tourist places like Joranda, Kapilash Temple etc.



2

Improvement such as widening & strengthening to defunct NH-53 from 306/650 Km to 310/700 Km (Parjanga Town Road) in the District of Dhenkanal.

Key Features:	<ul style="list-style-type: none"> Road Length: 4.05 km
Project Cost:	9.82 Crores
Completion Date:	30.08.2024
Agency:	<ul style="list-style-type: none"> P. K Pradhan & Co
Benefits of the Project:	<ul style="list-style-type: none"> This road is the defunct NH-53 passing through Parjanga Town. The market area of Parjanga Town is developed due to improvement of this road. BT & CC Road completed , Drain with other finishing works are balance.



3

Improvement to such as Widening & Strengthening of Dhenkanal-Kamakhyanagar Road from 0/000 km to 29/150 km (DLPS) in the District of Dhenkanal

Key Features:	<ul style="list-style-type: none"> Road length: 29.15 km
Project Cost:	24.99 Crores
Target Completion Date:	30.08.2024
Agency:	<ul style="list-style-type: none"> M/S R.K Associates
Benefits of the Project:	<ul style="list-style-type: none"> Due to improvement of this road to DLPS , the communication facility from NH-55 to NH-53 via Kamakshya Nagar has been improved.



4

Improvement to Joranda-Karamula Road (ODR) from 0/0 Km to 8/0 Krn in the District of Dhenkanal under NABARD Assistance.

Key Features:	<ul style="list-style-type: none"> Road length: 8 km
Project Cost:	10.21 Crores
Completion Date:	30.03.2025
Agency:	<ul style="list-style-type: none"> M/S Monalisa Construction

Benefits of the Project:	<ul style="list-style-type: none"> Due to improvement of this road to DLPS , the communication facility to tourist place Mahimagadi Joranda.
---------------------------------	---



Improvement to Joranda-Karmula Road (ODR) from 0/0km to 8/0km in the district of Dhenkanal under NABARD Assistance for the year 2021-2022



Improvement to Joranda-Karmula Road (ODR) from 0/0km to 8/0km in the district of Dhenkanal under NABARD Assistance for the year 2021-2022

5

Improvement such as widening & strengthening to defunct NH-53 from 350/225 Km to 355/150 Km (Kamakhya Nagar Town Road) in the District of Dhenkanal

Key Features:	<ul style="list-style-type: none"> Road length: 4.925 km
Project Cost:	16.82 Crores
Completion Date:	30.08.2024
Agency:	<ul style="list-style-type: none"> M/s S.K Agrawal



Benefits of the Project:	<ul style="list-style-type: none"> Due to improvement of this road to DLPS , the communication facility in Kamakshya Nagar town has been improved.
---------------------------------	---



6

Improvement to Bidharpur-Joranda Road from 0/0 Km to 10/760 Km for the year 2022-23 .

Key Features:	<ul style="list-style-type: none"> Road length: 10.76 km
Project Cost:	13.99 Crores
Completion Date:	30.09.2024
Agency:	<ul style="list-style-type: none"> Pradeep Kumar Pradhan



Improvement to Bidharpur-Joranda Road from 0/0 to 10/760km in the district of Dhenkanal under NABARD Assistance



Improvement to Bidharpur-Joranda Road from 0/0 to 10/760km in the district of Dhenkanal under NABARD Assistance

Benefits of the Project:

- Due to improvement of this road to DLPS , the communication facility in the tourist place Mahimagadi and also to Block headquarter.

7

Improvement to Mandar Bhaliapat chhak via Digambarpur from 0/0 km to 9/000 km for the year 2022-23 (XXVIII) .

Key Features:	<ul style="list-style-type: none"> Road length: 9 km
Project Cost:	12.00 Crores
Completion Date:	11.11.2024
Agency:	<ul style="list-style-type: none"> Sarat Ku Mishra



Benefits of the Project:	<ul style="list-style-type: none"> Due to improvement of this road to DLPS , the communication facility Block headquarter.
---------------------------------	---



8

Improvement to such as Widening & Strengthening of Gulehi-Nimabahali Road from 0/0 km to 19//050 km for the year 2022-23.

Key Features:	<ul style="list-style-type: none">• Road length: 19.5 km
Project Cost:	23.14 Crores
Completion Date:	08.04.2025
Agency:	<ul style="list-style-type: none">• SCS const. India PVT. LTD
Benefits of the Project:	<ul style="list-style-type: none">• Due to improvement of this road to DLPS , the communication facility Block headquarter.



9

Improvement such as widening & strengthening to Gudiakateni to Hindol road from 0/00 km to 29/480Km.

Key Features:	<ul style="list-style-type: none">• Road length: 29.84 km
Project Cost:	62.05 Crores
Completion Date:	22.01.2025
Agency:	<ul style="list-style-type: none">• M/S Ashirbad Engineer & Construction Pvt. Ltd.LTD
Benefits of the Project:	<ul style="list-style-type: none">• Due to improvement of this road to DLPS , the communication facility Block headquarter and Industrial area



10

Improvement such as widening and strengthening of Telibhuin - Giridhariprasad road 0/0km to 11/255km.

Key Features:	.Road length: 11.225 km
Project Cost:	13.49 Crores
Completion Date:	31.05.2025
Agency:	<ul style="list-style-type: none">• M/S Monalisa Construction

Benefits of the Project:	<ul style="list-style-type: none">• Due to improvement of this road to DLPS , the communication facility Block headquarter
---------------------------------	--



Construction of office building Boundary Wall & approach road at CT & GST Circle office Dhenkanal.

Scope of Work	Construction of an Double Storied Building for CT & GST Circle Office at Dhenkanal
Project Cost:	2.41 Crores
Completion Date:	30.10.2023
Agency:	<ul style="list-style-type: none">Ashok Kumar Guru

Benefits of the Project:

- This building helps in providing smooth functioning of Circle Office of CT & GST.



Construction of 100 bedded Boys Hostel Building in Odisha Adrasha Bidyalaya at Nizigarh, Hindol in the District of Dhenkanal for the year 2023-24.

Scope of Work	Construction of 100 bedded Boys Hostel Building in Odisha Adrash Bidyalaya at Nizigarh, Hindol in the District of Dhenkanal for the year 2023-24.
Project Cost:	4.63 Crores
Completion Date:	30.04.2025
Agency:	<ul style="list-style-type: none">Abhishek Kaliprasanna Puhan



Construction of 100 bedded Boys Hostel Building in Odisha Adrash Bidyalaya at Ankrantipur (Tentuliapada) under Odapada block in the District of Dhenkanal for the year 2023-24.

Scope of Work	Construction of 100 bedded Boys Hostel Building in Odisha Adrash Bidyalaya at Ankrantipur (Tentuliapada) under Odapada block in the District of Dhenkanal for the year 2023-24.
Project Cost:	4.42 Crores
Completion Date:	04.11.2024
Agency:	<ul style="list-style-type: none"> M/S Ananda Engg.



OnePlus 12

HASSELBLAD

● 23mm f/1.6 1/2053s ISO50
